Thamesview House Bulletin 7th July 2023



WEEKLY UPDATE WITH PHOTOS For week commencing 10th July 2023

- Fifth Floor, Core A has now been poured
- The columns and walls to Core A from Fifth Floor to Sixth Floor are in progress
- The columns and walls to Core B from Fourth to Fifth Floor are now complete
- The decking and Reinforcement to the Fifth Floor, Core B is in progress
- Tarmac to external areas is now complete
- We are continuing with the installation of the precast concrete stairs to both Core A and B
- Brickwork/blockwork has now commenced
- Scaffolders and materials are now on site and scaffolding will start to go up from next week
- We have employed a new Traffic Marshal who started on site on Monday 26th of June. He
 has been fully briefed on the traffic management plan and the importance of adhering to the
 correct directional flow of traffic. The current traffic management plan is to bring vehicles
 down Russell Road when approaching site and send vehicles up Sunbury Lane when
 leaving site. Following the traffic marshal starting there seems to be an improvement to the
 site entrance and the flow of traffic
- Litter picking of the surrounding roads is now taking place daily. We aim to get all our subcontractors involved in this process to stress the importance of keeping the local community clean
- Please note, site will be open on Saturday 8th July. Permitted working hours are 8am 1pm



Tony Johnson Senior Site Manager

Contact our Social Value and Community Team

- 0800 032 6760 (free phone) 8am to 8pm, seven days a week
- The Powder House
 Gunpowder Mill
 Powdermill Lane
 Waltham Abbey
 Essex, EN9 1BN



Thamesview House Bulletin 7th July 2023






External Area



First Floor Back Propping Removed



Fourth Floor Slab

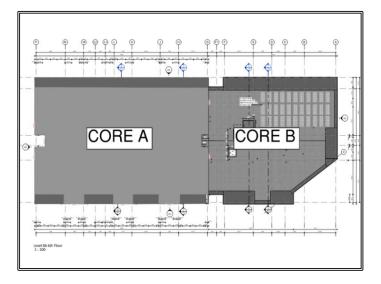

Core Identification



Tony Johnson Senior Site Manager

Contact our Social Value and Community Team

- 2 0800 032 6760 (free phone) 8am to 8pm, seven days a week
- The Powder House Gunpowder Mill Powdermill Lane Waltham Abbey Essex, EN9 1BN

