

WEEKLY UPDATE WITH PHOTOS

For week commencing 11th September 2023

- Ninth and Final floor slab are complete with just the upstands nearing completion.
- The framework contractor is now starting to decant from site with collections being booked daily.
- The scaffolder has completed the Fifth-floor scaffold and has commenced the Sixth floor following the completion of the loading bay the 5th floor.
- Steel frame is continuing and has progressed with Ground, First, Second, Third, Fourth and Fifth Floors boarded.
- Steel frame to the 6th floor has now commenced.
- Window installation is now complete to the Ground and First, Second and Third Floors.
- Precast concrete stairs to Core A and B are now complete.
- Blockwork is now complete to the Ground, First, Second, Third and Fourth Floors the 6th floor has commenced.
- External brickwork has now commenced to the Ground Floor following the damp proof membrane and insulation installed.
- Mechanical and Electrical works have now started on site and are continuing up the building.
- Demolition to the two garage areas is now complete and now available for parking.
- The internal drylining has now started on site with loading out of the materials and the setting out to the apartments.
- Please note, site will not be open on Saturday 09/09/2023.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

📍 The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN




Thamesview House Bulletin

11th September 2023




1st Floor Drylining Commenced

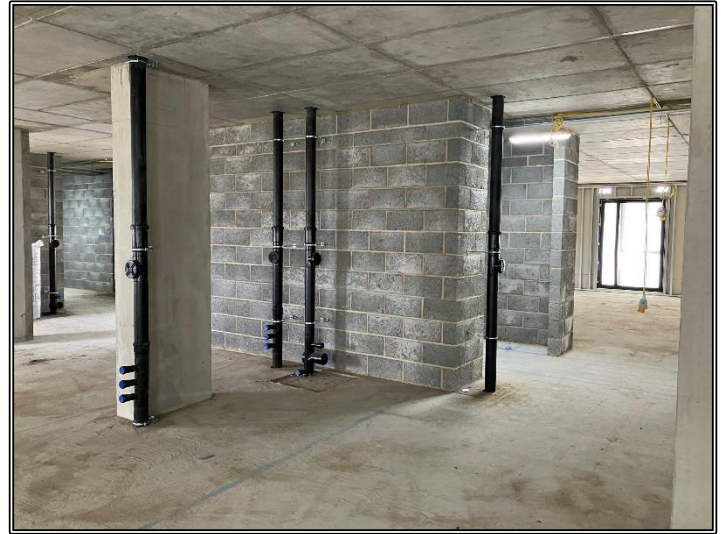

3rd Floor Mechanical Pipework



4th Floor Steel Frame

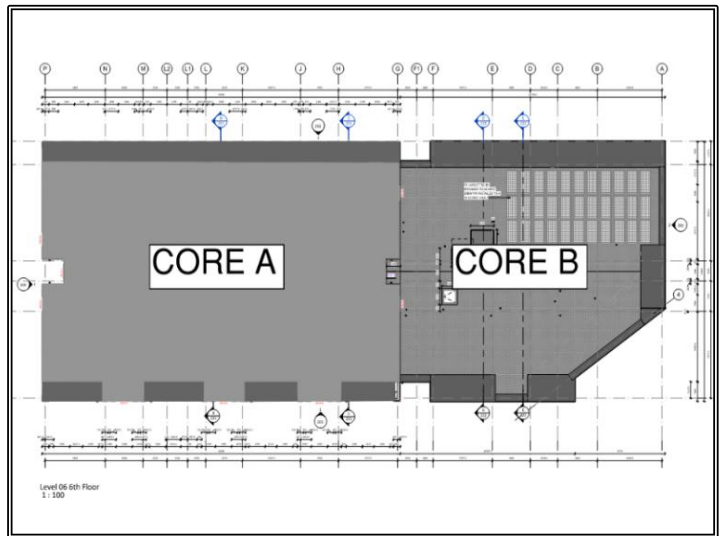

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

