

WEEKLY UPDATE WITH PHOTOS

For week commencing 18th September 2023

- The concrete frame has now been completed.
- The concrete frame contractor continues to strike all formwork with all materials removed from site by week commencing 25/09/2023.
- The scaffolding to the Sixth Floor has been completed.
- Steel frame to the external walls has continued to the Sixth Floor this week.
- The window installation to the Fourth Floor has commenced.
- We have now commenced the party wall drylining to the First Floor.
- We have continued the blockwork to the mechanical and electrical risers to the Sixth Floor.
- The external brickwork has continued this week with the Ground Floor to First Floor now half way.
- We have commenced the installation of the ventilation ducting to the First Floor.
- We have now commenced the heating and water distribution pipework.
- The internal drylining has now started on site with loading out of the materials and the setting out to the apartments.
- We have commenced the internal insulation to the external walls.
- The site will be open on Saturday 16/09/2023 between 8am and 1pm.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

📍 The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN



Thamesview House Bulletin

15th September 2023




1st Floor Ventilation Installation



1st Floor Drylining



4th Floor Window Installation

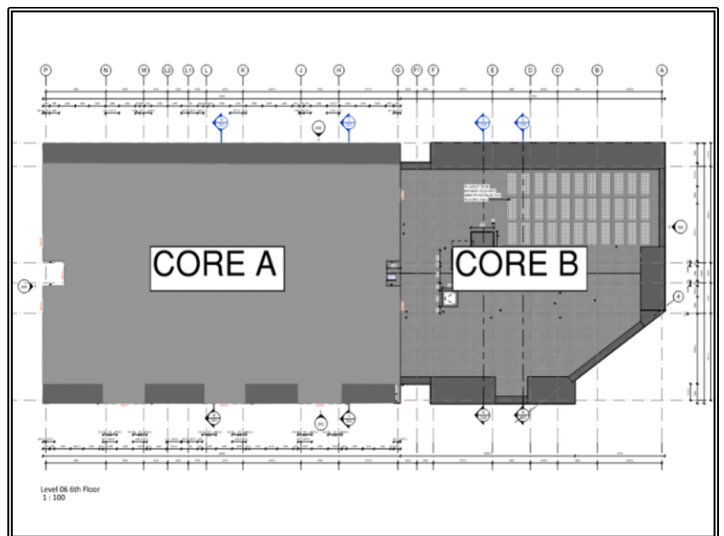

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

