

WEEKLY UPDATE WITH PHOTOS

For week commencing 25th September 2023

- The concrete frame contractor continues to strike all formwork with all materials removed from site by week commencing 25/09/2023.
- The scaffolding to the Seventh Floor has continued this week and is due to be completed next week.
- Steel frame to the external walls has continued to the sixth floor this week.
- The window installation to the fourth floor has been completed.
- The party wall install is nearing completion. Second and third floor party wall install has commenced.
- Screeding to the first floor is due commence next week.
- We have commenced the blockwork to the mechanical and electrical risers to the seventh floor.
- The external brickwork has continued this week with the ground floor to first floor now up to lintel height.
- Ventilation flat ducting install to the first floor has been completed. Ground and second floor has commenced.
- We will continue the heating and water distribution pipework installation.
- We have commenced the internal insulation to the external walls.
- Electrical wiring is due to commence next week.
- The site will be open on Saturday 23/09/2023 between 8am and 1pm.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN



Thamesview House Bulletin

25th September 2023

Resident Drop in session

All welcome to attend our next session:


Date: Wednesday 27th September Time: 4pm- 6pm Location: Site office




Ground Floor Brickwork



1st Floor Party Walls

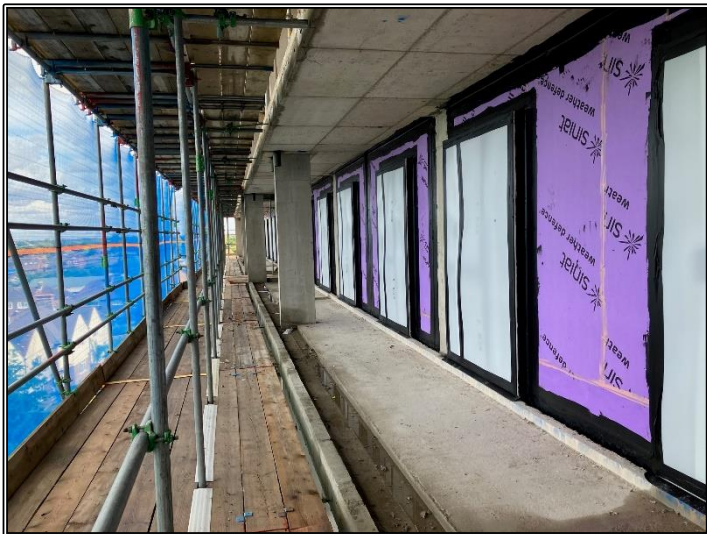

4th Floor Windows Complete

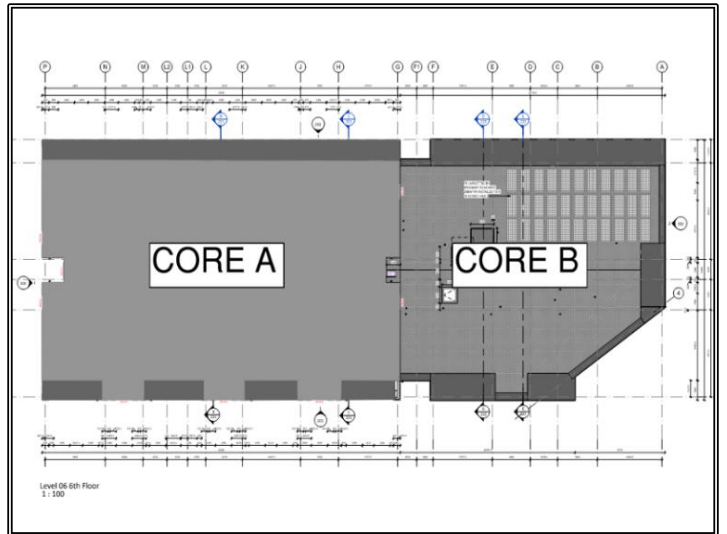

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

