Thamesview House Bulletin 2nd October 2023



WEEKLY UPDATE WITH PHOTOS For week commencing 2nd October 2023

- The concrete frame contractor continues to carry out the remaining making good progress.
- The scaffolding to the seventh floor has now been completed.
- Steel frame to the external walls has continued to the sixth floor is now nearing completion.
- The window installation to the fourth floor has been completed and fifth floor window are due to be started this week.
- The first floor party wall install is nearing completion. second and third floor party wall install
 has commenced and is ongoing.
- Screeding to the first floor is now in progress with the insulation being installed.
- We have commenced the blockwork to the mechanical and electrical risers to the seventh floor and is due to be completed this week.
- The external brickwork has continued this week with the ground floor to first floor now up to lintel height and the lintels are now being built in.
- Ventilation flat ducting installation to the first floor has been completed. Ground and second floor installation is ongoing.
- We will continue the heating and water distribution pipework installation.
- We have commenced the internal insulation to the external walls and first fix studwork is in progress.
- Electrical wiring has now commenced on site.
- The site will be open on Saturday 30/09/2023 between 8am and 1pm.



Tony Johnson Senior Site Manager

Contact our Social Value and Community Team

- 0800 032 6760 (free phone) 8am to 8pm, seven days a week
- The Powder House
 Gunpowder Mill
 Powdermill Lane
 Waltham Abbey
 Essex, EN9 1BN



Thamesview House Bulletin 2nd October 2023








1st Floor Drylining

1st Floor Screed Insulation



6th Floor Boarding

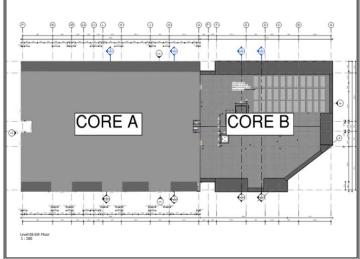

Core Identification



Tony Johnson Senior Site Manager

Contact our Social Value and Community Team

- 2 0800 032 6760 (free phone) 8am to 8pm, seven days a week
- The Powder House
 Gunpowder Mill
 Powdermill Lane
 Waltham Abbey
 Essex, EN9 1BN

