

WEEKLY UPDATE WITH PHOTOS

For week commencing 27th November 2023

- The scaffolding to the seventh floor has now been completed and progressing to the eighth floor. Sixth and seventh floors loading bay are now complete and they are currently carrying out adaptations for the lower levels.
- Steel frame to the external walls has been completed to the seventh and eighth floors and are now boarded.
- The window installation is now complete.
- Ground to sixth floor party walls is now complete with the seventh floor in progress.
- Screeding from first to fifth floor is now complete with the sixth floor in progress.
- We have completed the blockwork to the mechanical and electrical risers.
- The external brickwork has continued this week with the ground floor to first floor completed. First and second floor is in progress.
- Ventilation flat ducting to all levels is now complete.
- We will continue installation of the heating and water pipework, progressing to the second floor first fix which will be handed over this week.
- The internal insulation to the external walls is now complete.
- Electrical wiring is progressing on site and containment to the communal areas is in progress and now being worked on within the second floor and progressed to the third floor.
- The site will be open on Saturday 25/11/2023 between 8am and 1pm.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

📍 The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN



Thamesview House Bulletin


27th November 2023



7th Floor Party Walls



6th Floor Screed Insulation

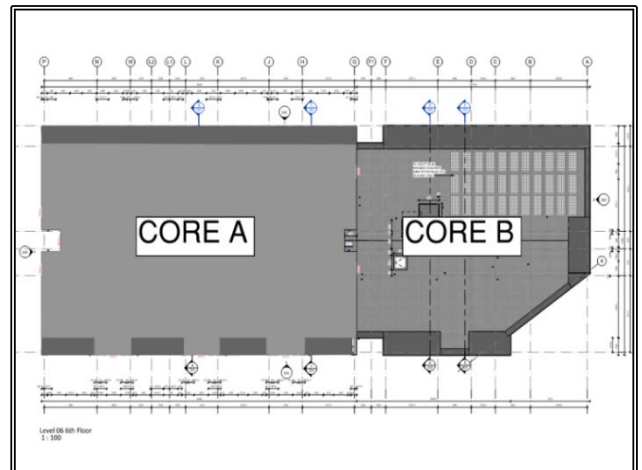

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

