

WEEKLY UPDATE WITH PHOTOS

For week commencing 15th January 2024

- The scaffolding to the seventh floor has now been completed and progressing to the eighth floor. Sixth and seventh floors loading bay are now complete and they are currently carrying out adaptations for the lower levels.
- Steel frame to the external walls have been completed to the seventh and eighth floors and are now boarded.
- Ground to seventh floor party walls are now complete with the eighth floor in progress.
- Screeding from first to sixth floor is now complete with the seventh floor completing on the 11/01/2024.
- Screed to the ground floor is now complete.
- We have completed the blockwork to the mechanical and electrical risers.
- The external brickwork has not taken place this week due to the adverse low temperatures but the bricklayers have continued with the masonry support and insulation.
- Ventilation flat ducting to all levels is now complete.
- We will continue the heating and water distribution pipework installation and first fix has continued to first and second floor. Third floor is also in progress.
- The external insulation is now progressing to the fourth floor and fifth floor.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN



Thamesview House Bulletin

15th January 2024

- The site will not be open on Saturday 13/01/2024.




6th Floor Roof Insulation



6th Floor Drylining First Fix



8th Floor Party Walls

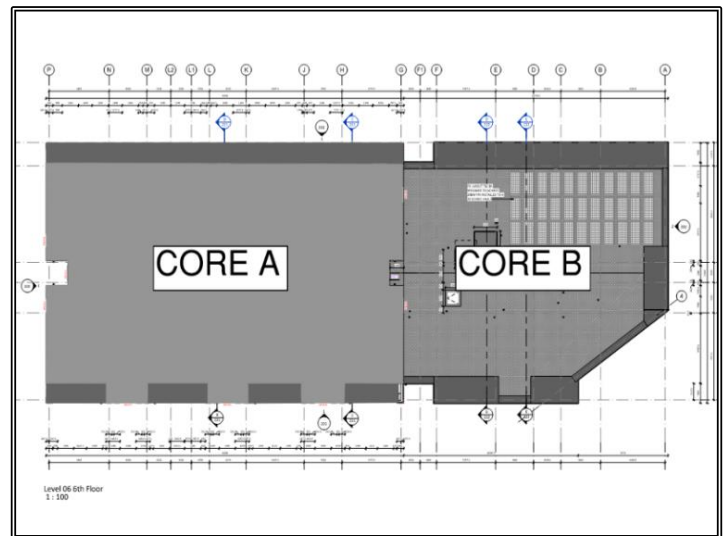

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

📍 The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

