

WEEKLY UPDATE WITH PHOTOS

For week commencing 29th January 2024

- Steel frame to the external walls has been completed to the seventh and eighth floors and are now boarded.
- Ground to seventh floor party walls are now complete with the eighth-floor nearing completion.
- Screeding from ground to seventh floors are complete. Eighth floor is due to be completed this week.
- We have completed the blockwork to the mechanical and electrical risers.
- The external brickwork has recommenced following the recent bad weather, we are now progressing the third to fourth floors.
- Ventilation flat ducting to all levels is now complete.
- We will continue the heating and water pipework installation and have completed floors 1- 5. sixth floor is in progress.
- The external insulation is now complete to the fourth floor with fifth floor in progress.
- Electrical wiring is progressing on site and containment to the communal areas is in progress.
- The site will be open on Saturday 27/01/2024 between 8am and 1pm.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week


✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN




Thamesview House Bulletin


29th January 2024

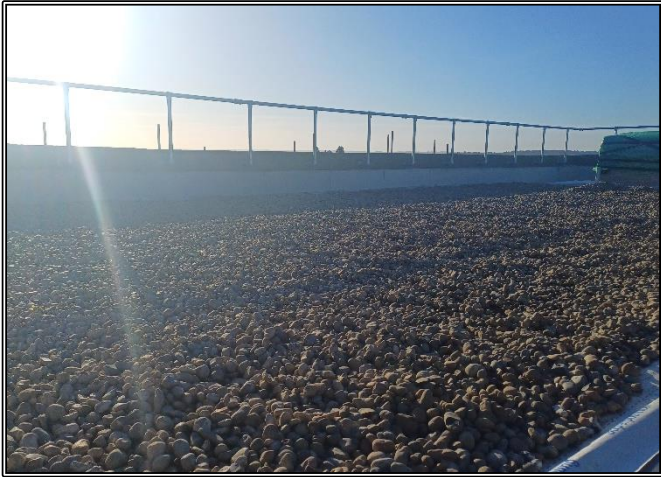


8th Roof Pebbles

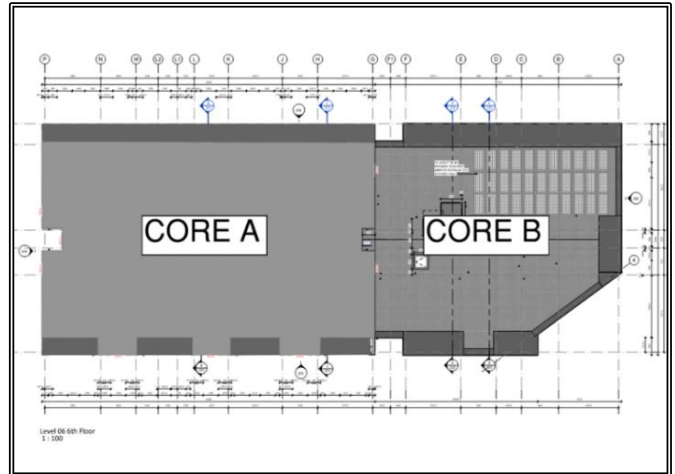

Core Identification

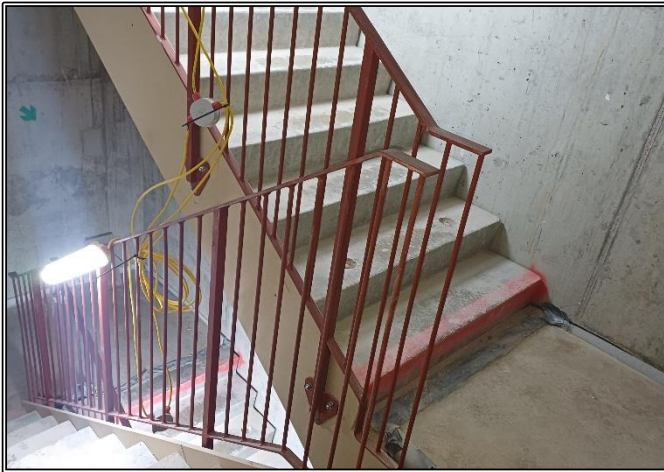

Core A Handrails Installed

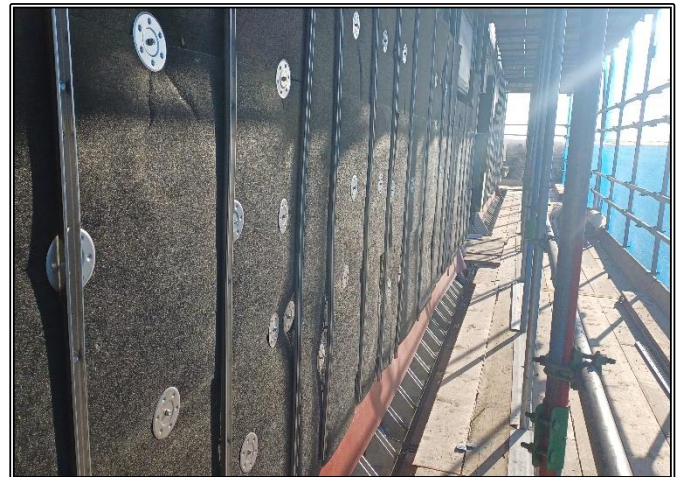

5th Floor External Insulation and Masonry Supports



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

