

## WEEKLY UPDATE WITH PHOTOS For week commencing 19<sup>th</sup> February 2024

- Steel frame to the external walls has been completed to the seventh and eighth floors.
- Ground to eighth floor party walls are now complete.
- Screeding from ground to eighth floors are complete.
- Sand and cement screed to the ground floors will follow.
- We have completed the blockwork to the mechanical and electrical risers with plant room.
- Bin store block walls in progress.
- The external brickwork has now progressed, and we are now nearing completion on the third floor.
- Ventilation flat ducting to all levels is now complete.
- Heating and water distribution pipework installation has been completed to the seventh floor.
- The external insulation is now complete to the fourth floor with fifth floor in progress.
- Internal doors and frames are being fitted and are currently complete to the second floor.
- Kitchen installations have now commenced, with completion nearing on the first floor.
- Core B lift has been installed with core A starting this coming week.



**Tony Johnson**  
Senior Site Manager

### Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House  
Gunpowder Mill  
Powdermill Lane  
Waltham Abbey  
Essex, EN9 1BN



# Thamesview House Bulletin

## 19<sup>th</sup> February 2024


- The site will be open on Saturday 17/02/2024 between 8am and 1pm.




*1<sup>st</sup> Floor Kitchens*



*1<sup>st</sup> Floor Baths*

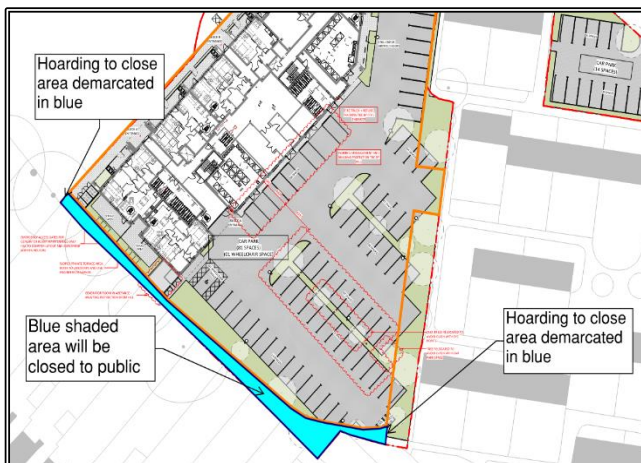

*Hoarding Change*

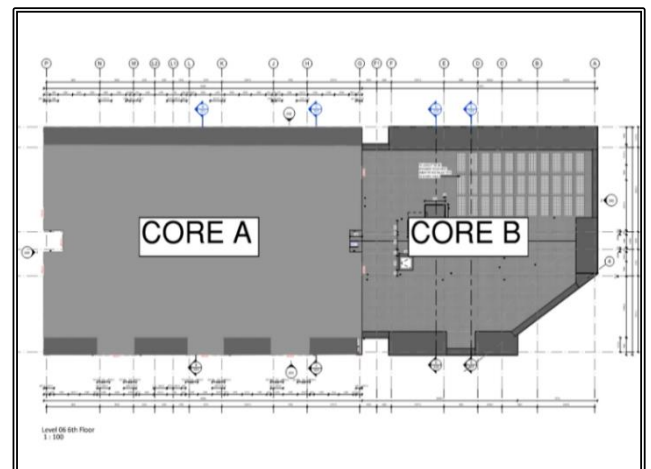

*Core Identification*



**Tony Johnson**  
Senior Site Manager

### Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House  
Gunpowder Mill  
Powdermill Lane  
Waltham Abbey  
Essex, EN9 1BN

CONSIDERATE  
CONSTRUCTORS  
SCHEME

