

WEEKLY UPDATE WITH PHOTOS For week commencing 18th March 2024

- Ground to Eighth floor party walls are now complete.
- Screeding from ground to Eighth floors are complete.
- Sand and cement screed to the ground floors will follow later.
- The external brickwork has now progressed to the Fifth and Sixth floors.
- We will continue the heating and water distribution pipework installation which has been completed to the Eighth floor.
- Buffer vessels and pumps are now on site and in position in anticipation of the plant rooms works commencing.
- The external insulation is now complete to the Fifth floor with Sixth floor nearing completion.
- Electrical second fix has now started on the First floor.
- Solar panels are now in position on the Eighth floor roof.
- Internal doors and frames are being fitted and are currently complete to the Third floor.
- Kitchen installations have now started, and now completed to the Second floor. The Third floor installation is now in progress.
- Core B lift has been installed with Core A progressing well.
- Tiling to kitchens and bathrooms are complete to the First floor and due to progress to the Second floor this coming week.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN



Thamesview House Bulletin

18th March 2024


- The site will not be open on Saturday 16/03/2024 due to the M25 being closed in both directions over the weekend between 8am and 1pm.




Buffer Vessels On Site



1st Floor Electrical 2nd Fix

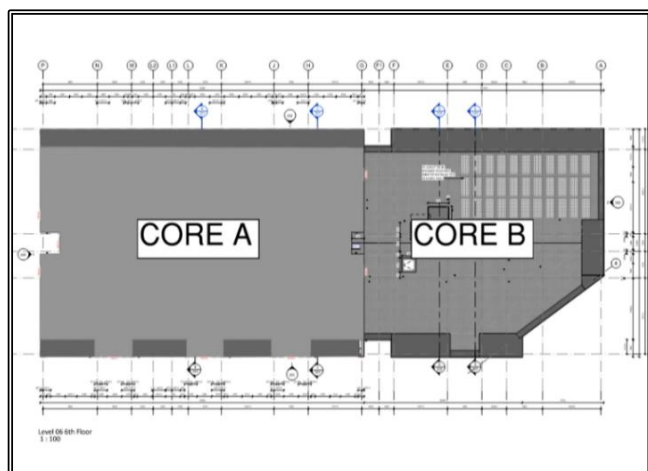

Core Identification

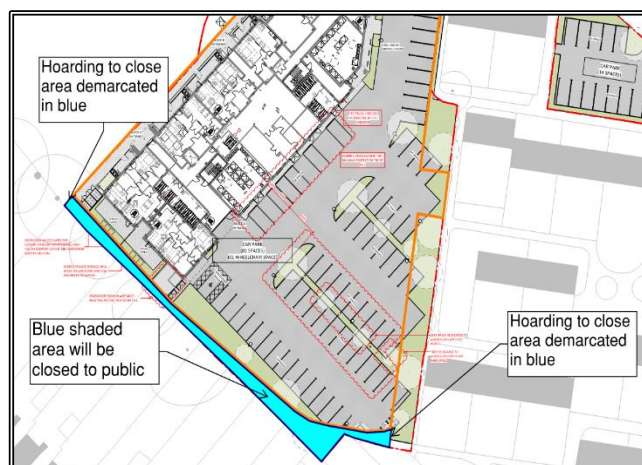

Hoarding Change



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

**CONSIDERATE
CONSTRUCTORS
SCHEME**

