
WEEKLY UPDATE WITH PHOTOS


For week commencing 15th April 2024

- Core B external brickwork is complete on the Sixth floor and Seventh floor on Core A.
- The communal walls have been closed on the First, Second and Third floors with the Fourth floor in progress.
- Tape and Jointing has now commenced on the Seventh floor.
- The plant room works are now in progress.
- The external insulation is now complete to the Seventh floor.
- Electrical second fix has progressed up to the Fifth floor.
- Solar panels are now in position on the Sixth & Ninth floor roof.
- The air source heat pumps are installed on the Ninth-floor roof.
- Internal doors and frames are being fitted to the Fourth & Fifth floors.
- Kitchen installation is complete to the Fourth floor. Fifth floor is now 50% complete.
- Core A lift installation is progressing well.
- Tiling to kitchens and bathrooms are complete to the First and Second floors now progressing on the Third floor now 50% complete.
- The site will be open on Saturday 13/04/2024.




Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

 0800 032 6760 (free phone) 8am to 8pm, seven days a week

 residents@hill.co.uk

 The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN



Thamesview House Bulletin

15th April 2024




6th Floor Brickwork Complete



GF Plant Room Containment



Fire Alarm Test 10/04/2024

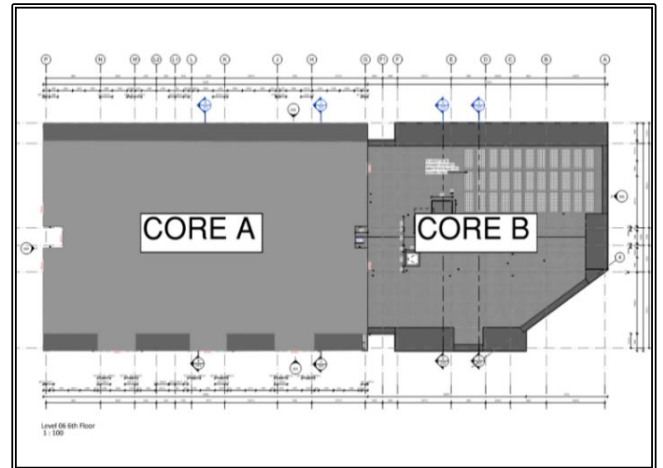

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

📍 The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

