

### WEEKLY UPDATE WITH PHOTOS

#### For week commencing 22<sup>nd</sup> April 2024

- Core B external brickwork is complete and Core A brickwork is progressing on the Seventh floor.
- The communal walls have been closed on the First, Second and Third floor with the Fourth floor in progress.
- Tape and jointing has now commenced on the Eighth floor.
- The plant room works are in progress.
- The external insulation is in progress on the Seventh floor.
- Electrical second fix has progressed up to the Sixth floor.
- Solar panels are now in position on the Sixth & Ninth floor roof.
- The air source heat pumps are installed on the Ninth floor roof.
- Internal doors and frames are being fitted to the Sixth floor.
- Kitchen installation is complete to the Fifth floor. Sixth floor is 50% complete.
- Core A lift installation is 50% complete.
- Tiling to kitchens and bathrooms are complete to the First and Second floors with the Third & Fourth floors in progress.
- The site will be open on Saturday 20/04/2024.



**Tony Johnson**  
Senior Site Manager

#### Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House  
Gunpowder Mill  
Powdermill Lane  
Waltham Abbey  
Essex, EN9 1BN



# Thamesview House Bulletin

22<sup>nd</sup> April 2024




1<sup>st</sup> Floor Benchmark Plot Latex



8<sup>th</sup> Floor Ceiling Close-Up



GF Plant Room Hot Water Boosters

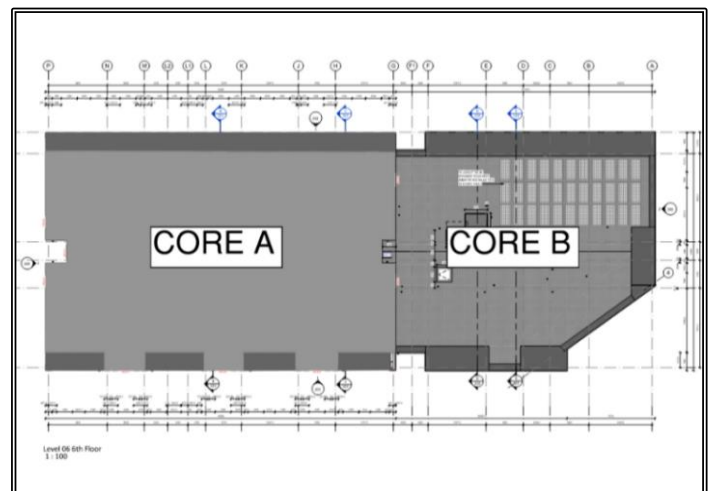

Core Identification



**Tony Johnson**  
Senior Site Manager

## Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

📍 The Powder House  
Gunpowder Mill  
Powdermill Lane  
Waltham Abbey  
Essex, EN9 1BN

