
WEEKLY UPDATE WITH PHOTOS

For week commencing 29th April 2024

- Core B External brickwork is complete and Core A brickwork is due to complete in the next period.
- The communal walls have been closed on the First, Second, Third and Fourth floors with the Fifth floor in progress.
- Tape and jointing has now commenced on the Eighth floor and nearing completion with Ground floor progressing in the next period.
- The plant room works are in progress.
- The external insulation is in progress on the Seventh floor and nearing completion.
- Electrical second fix has progressed up to the Seventh floor.
- Solar panels are now in position on the Sixth & Ninth floor roof.
- The air source heat pumps are installed on the Ninth-floor roof.
- Internal doors and frames are now fitted to the Sixth floor with Seventh in progress.
- Kitchen installation is complete to the Sixth floor. Seventh floor is in progress.
- Core A lift installation is on-going.
- Tiling to kitchens and bathrooms are complete to the First, Second and Third floors with the Fourth Floor in progress.
- The site will be open on Saturday 27/04/2024.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN



Thamesview House Bulletin

29th April 2024




7th Floor North-West Brickwork Complete



Substation On Site



Site Team Lunch In Celebration Of St George's Day

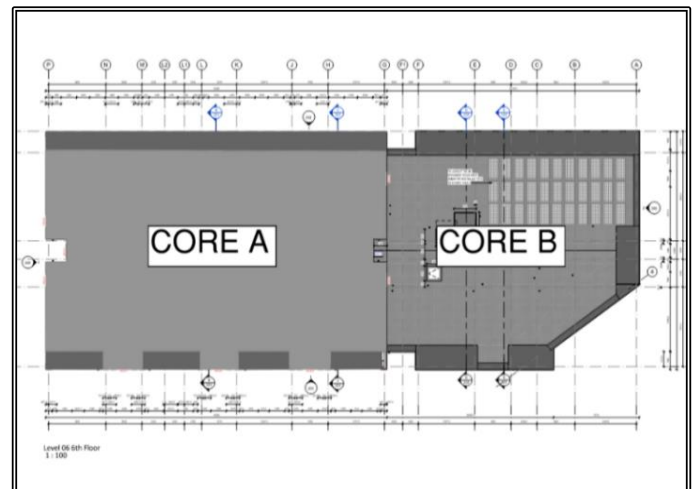

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

📍 The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

