

## WEEKLY UPDATE WITH PHOTOS For week commencing 31<sup>st</sup> July 2023

- Sixth floor slabs core A & B are now complete. Core B is now complete to its full height.
- The columns and walls to Core A from sixth floor to seventh floors are complete.
- Decking to seventh floor slab is complete and rebar is in progress.
- SFS framing is continuing and has progressed to the second floor with loading out continuing to the upper floors.
- Windows are now on site for both ground and first floors and fitting is booked for this week.
- We are continuing with the installation of the precast concrete stairs to both Core A and B.
- Brickwork/ blockwork is now continuing to the ground and first floors and progressing to the upper floors.
- Mechanical and electrical works have now started on site.
- We will begin fencing the remaining garage areas, on the Thamesmead Estate, during week commencing 31/07/2023 in preparation for the demolition works.
- Please note, site will be open on Saturday 29<sup>th</sup> July. The permitted working hours are 8am – 1pm.



Tony Johnson Senior Site Manager

## **Contact our Social Value and Community Team**

- 0800 032 6760 (free phone) 8am to 8pm, seven days a week
- residents@hill.co.uk
- The Powder House
  Gunpowder Mill
  Powdermill Lane
  Waltham Abbey
  Essex, EN9 1BN



## Thamesview House Bulletin 28<sup>th</sup> July 2023






First Floor Blockwork



External Wall Board



Fourth Floor Containment

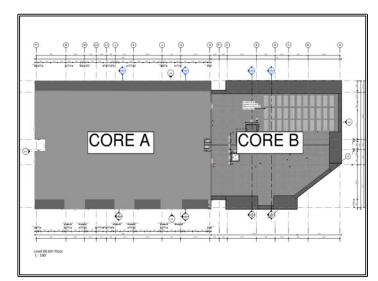

Core Identification



Tony Johnson Senior Site Manager

## **Contact our Social Value and Community Team**

- 0800 032 6760 (free phone) 8am to 8pm, seven days a week
- ⊠ residents@hill.co.uk
- The Powder House
  Gunpowder Mill
  Powdermill Lane
  Waltham Abbey
  Essex, EN9 1BN

