

WEEKLY UPDATE WITH PHOTOS

For week commencing 14th August 2023

- Vertical column from Seventh to Eighth Floor are complete.
- Eighth floor decking and rebar is complete, concrete to the slab due early next week.
- Steel frame is continuing and has progressed with Ground, First and Second floor boarded.
- Third Floor Steel frame has been completed with boarding to follow.
- Window installation is now complete to the Ground Floor
- Windows to the Second Floor are in progress.
- We are continuing with the installation of the precast concrete stairs to Core A and B.
- Blockwork is now complete to the Ground floor with First and Second Floors in progress.
- Mechanical and electrical works have now started on site and is continuing up the building.
- Demolition to the two garage areas are now complete.
- Please note, site will be open on Saturday 12/08/2023. The permitted working hours are 8am – 1pm.

On **Saturday 2nd September** the project team invites you to join us for a breakfast roll & a hot drink!

Find out more about the project and ask any questions you may have about the ongoing works. The hot food van will be positioned from **7:30am- 12:00pm** at the **main site entrance** to the Thamesview project.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN



Thamesview House Bulletin

14th August 2023




Garage Demolition Complete



Substation Door Installed



Window Install to the First Floor

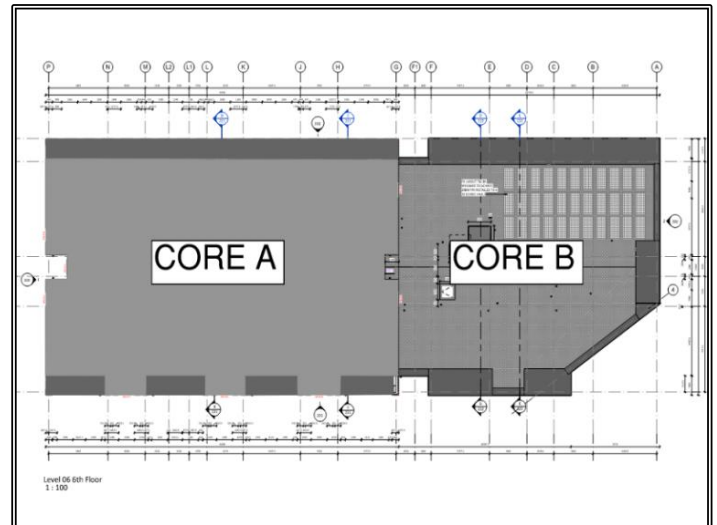

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

