

WEEKLY UPDATE WITH PHOTOS

For week commencing 21st August 2023

- Eighth Floor slab is now complete.
- Vertical columns to the Eighth Floor are nearing completion with the final decking now started.
- Steel frame is continuing and has progressed with Ground, First and Second Floors boarded.
- Third and Fourth Floor Steel frame has been completed with boarding to follow.
- Window installation is now complete to the Ground and First Floors.
- Precast concrete stairs to Core A and B are now complete.
- Blockwork is now complete to the Ground, First and Second Floors are complete with the higher floors progressing.
- Mechanical and electrical works have now started on site and is continuing up the building.
- Demolition to the two garage areas is now complete.
- Please note, site will be open on Saturday 19/08/2023. The permitted working hours are 8am – 1pm.

On **Saturday 2nd September** the project team invites you to join us for a breakfast roll & a hot drink!

Find out more about the project and ask any questions you may have about the ongoing works. The hot food van will be positioned from **7:30am- 12:00pm** at the **main site entrance** to the Thamesview project.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN




Thamesview House Bulletin


21st August 2023




First Floor Windows Complete

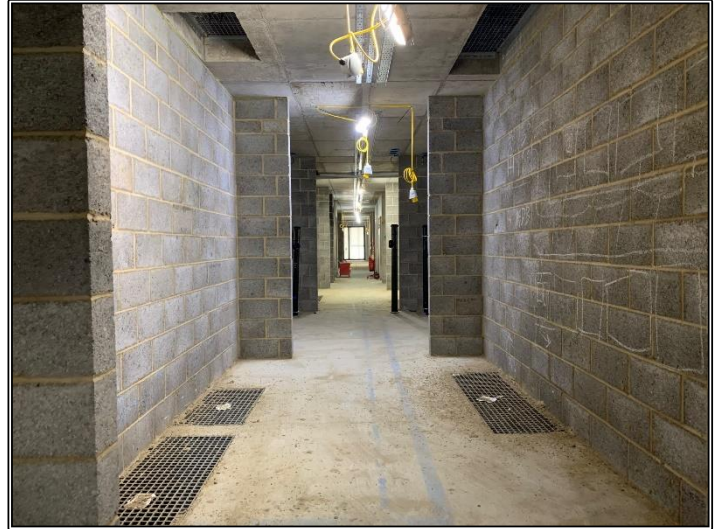

First Floor Blockwork Complete

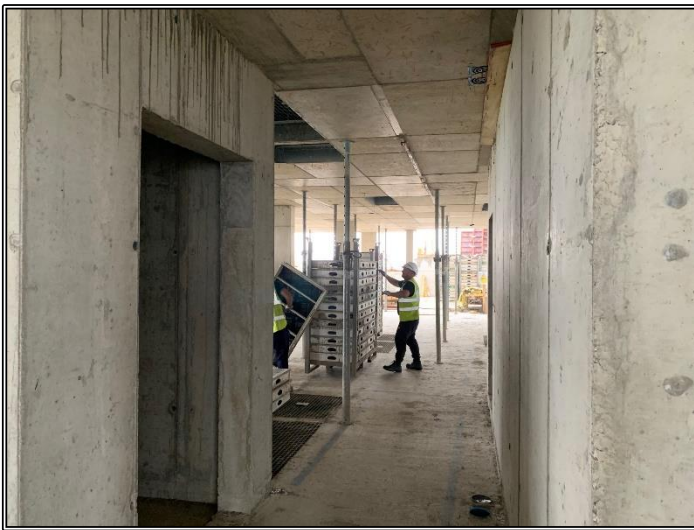

Sixth Floor Striking Complete

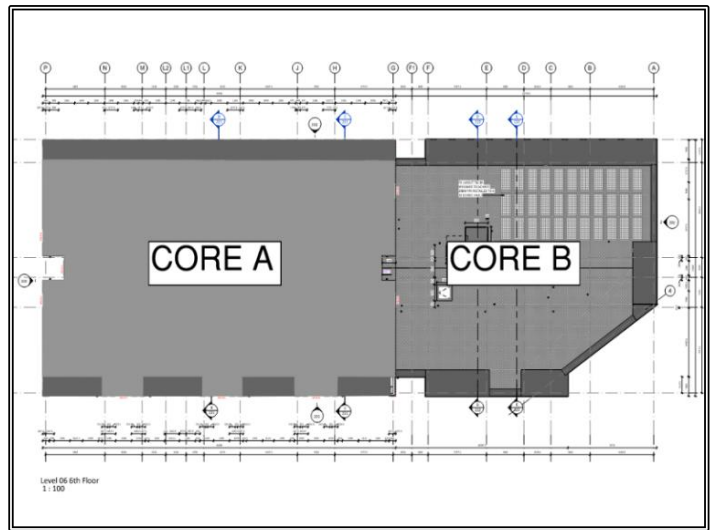

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

📍 The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

